ID	Task Name	Unit	Duration	Start	Finish	% Complete
1	Name of Work: Improvements to Burial Ground at Yelahanka and Kenchenahalli in Ward No.01 & 02 of Yelahanka Sub Division (PACKAGE-03)					0%
2	Mobilization		1 day	Tue 19-05-20	Tue 19-05-20	100%
3	Earthwork Excavation for Lowering and Lowering	Cum	60 days	Wed 20-05-20	Tue 11-08-20	100%
4	Earthwork Excavation by manual means for foundation	Cum	135 days	Mon 25-05-20	Fri 27-11-20	100%
5	Filling of broken metal of 100mm	Cum	120 days	Fri 29-05-20	Thu 12-11-20	100%
6	Plain Cement Concrete of mix 1:3:6	Cum	140 days	Fri 05-06-20	Thu 17-12-20	100%
7	TMT Steel of Fe500	Tonne	150 days	Wed 10-06-20	Tue 05-01-21	100%
8	Centering for Footing	Sqm	150 days	Wed 10-06-20	Tue 05-01-21	100%
9	Reinforced Cement Concrete of mix design M20	Cum	155 days	Mon 15-06-20	Fri 15-01-21	99%
10	Centering for Column	Sqm	150 days	Fri 12-06-20	Thu 07-01-21	100%
11	Size Stone Masonry for foundation	Cum	120 days	Thu 25-06-20	Wed 09-12-20	100%
12	Size Stone Masonry for Basement	Cum	120 days	Wed 01-07-20	Tue 15-12-20	100%
13	Flush Pointing for Size Stone Masonry	Sqm	125 days	Thu 25-06-20	Wed 16-12-20	100%
14	Refilling available earth	Cum	125 days	Tue 30-06-20	Mon 21-12-20	100%
15	Centering for Plinth Beam	Sqm	90 days	Sun 05-07-20	Thu 05-11-20	93%

Project: Burial Ground-Bar Chart
Date: Thu 04-02-21

Task	Project Summary	Inactive	
Split	External Tasks	Inactive	
Milestone	External Milestone	Manual	
Summary	Inactive Task	Duratio	

12

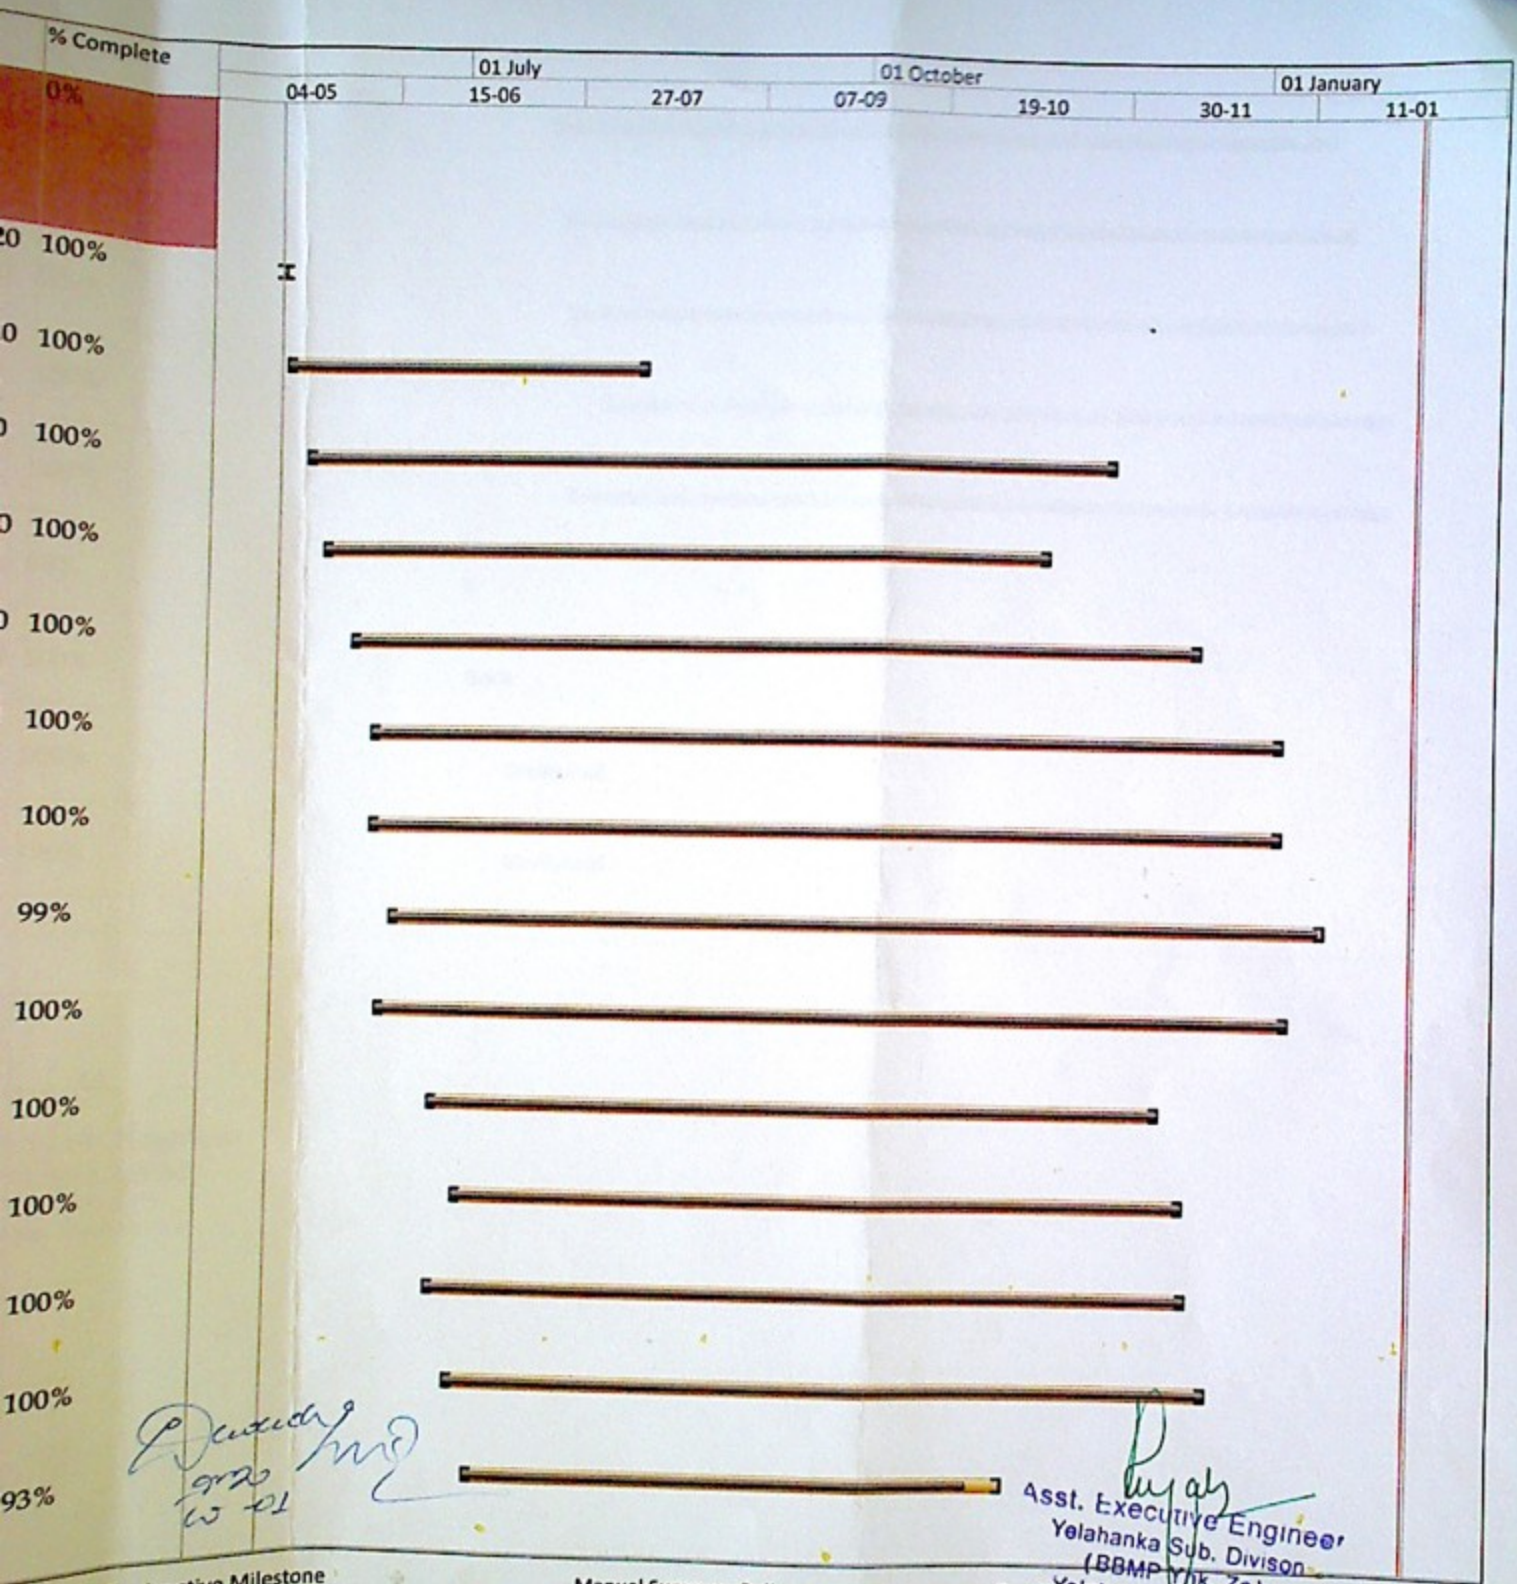

Asst. Executive Engineer
Yelahanka Sub. Divison
(BBMP Yk. Zn)
Yelahanka, Bangalore

ID	Task Name	Unit	Duration	Start	Finish	% Complete
16	Solid Concrete Blocks of Size 400x200x200mm	Sqm	130 days	Mon 20-07-20	Fri 15-01-21	100%
17	Plain Cement Concrete of mix 1:2:4	Cum	130 days	Thu 23-07-20	Wed 20-01-21	100%
18	20mm thick Cement Plastering	Sqm	132 days	Sat 25-07-20	Sun 24-01-21	100%
19	Painting in two coats	Sqm	131 days	Sun 02-08-20	Fri 29-01-21	100%
20	Hot Dip Galvanized Gate	sqm	136 days	Sat 25-07-20	Fri 29-01-21	100%
21	Sinking of Borewell of 165mm dia	m	2 days	Thu 02-07-20	Fri 03-07-20	90%
22	Submersible Pump Sets of 150mm dia	Nos	7 days	Fri 03-07-20	Mon 13-07-20	100%
23	Electric Work for Borewell	Nos	17 days	Mon 13-07-20	Tue 04-08-20	100%
24	Plumbling Work	m	17 days	Mon 13-07-20	Tue 04-08-20	100%

04-05

15-01

Asst. Executive Engineer
Yelahanka Sub. Divison
(BBMP Ynk. Zn)
Yelahanka, Bangalore

Project: Burial Ground-Bar Chart
Date: Thu 04-02-21

Task	Project Summary	Inactive Milesto
Split	External Tasks	Inactive Summa
Milestone	External Milestone	Manual Task
Summary	Inactive Task	Duration-only

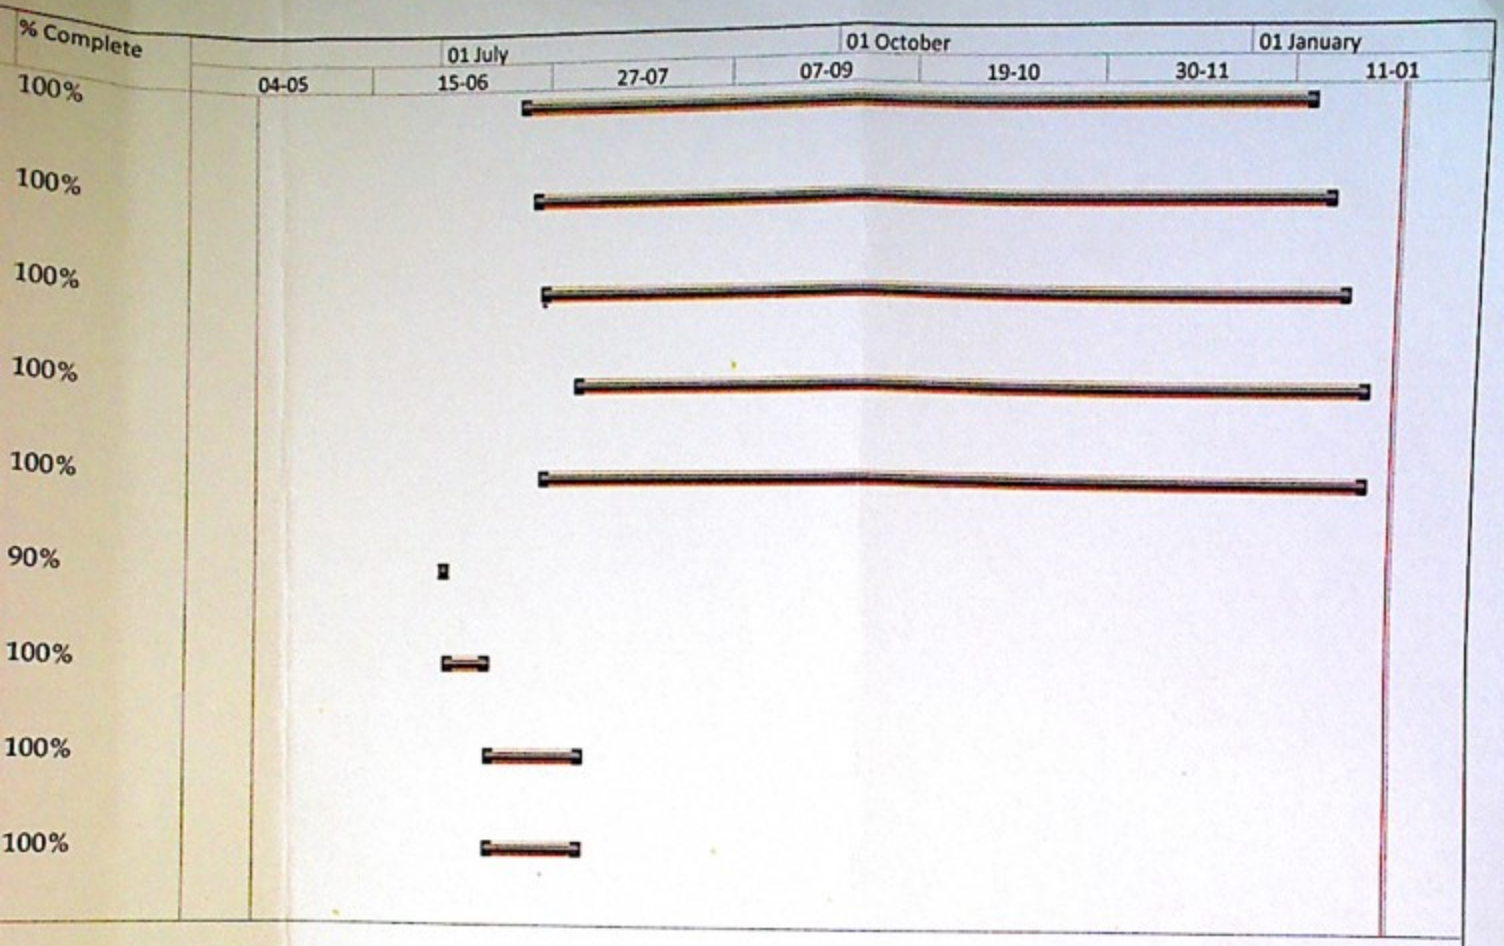

ecutive Engineer
ka Sub. Divison
MP Ynk. Zn)
nka. Bangalore

Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
